

Cumberland Valley School District



MOUNTAIN VIEW MIDDLE SCHOOL & SITE WORK

CONSTRUCTION UPDATE

November 3, 2017



CRABTREE, ROHRBAUGH & ASSOCIATES
ARCHITECTS



Massaro
CONSTRUCTION MANAGEMENT SERVICES, LLC


Roundabout



Paving & line striping of the Roundabout




Roundabout

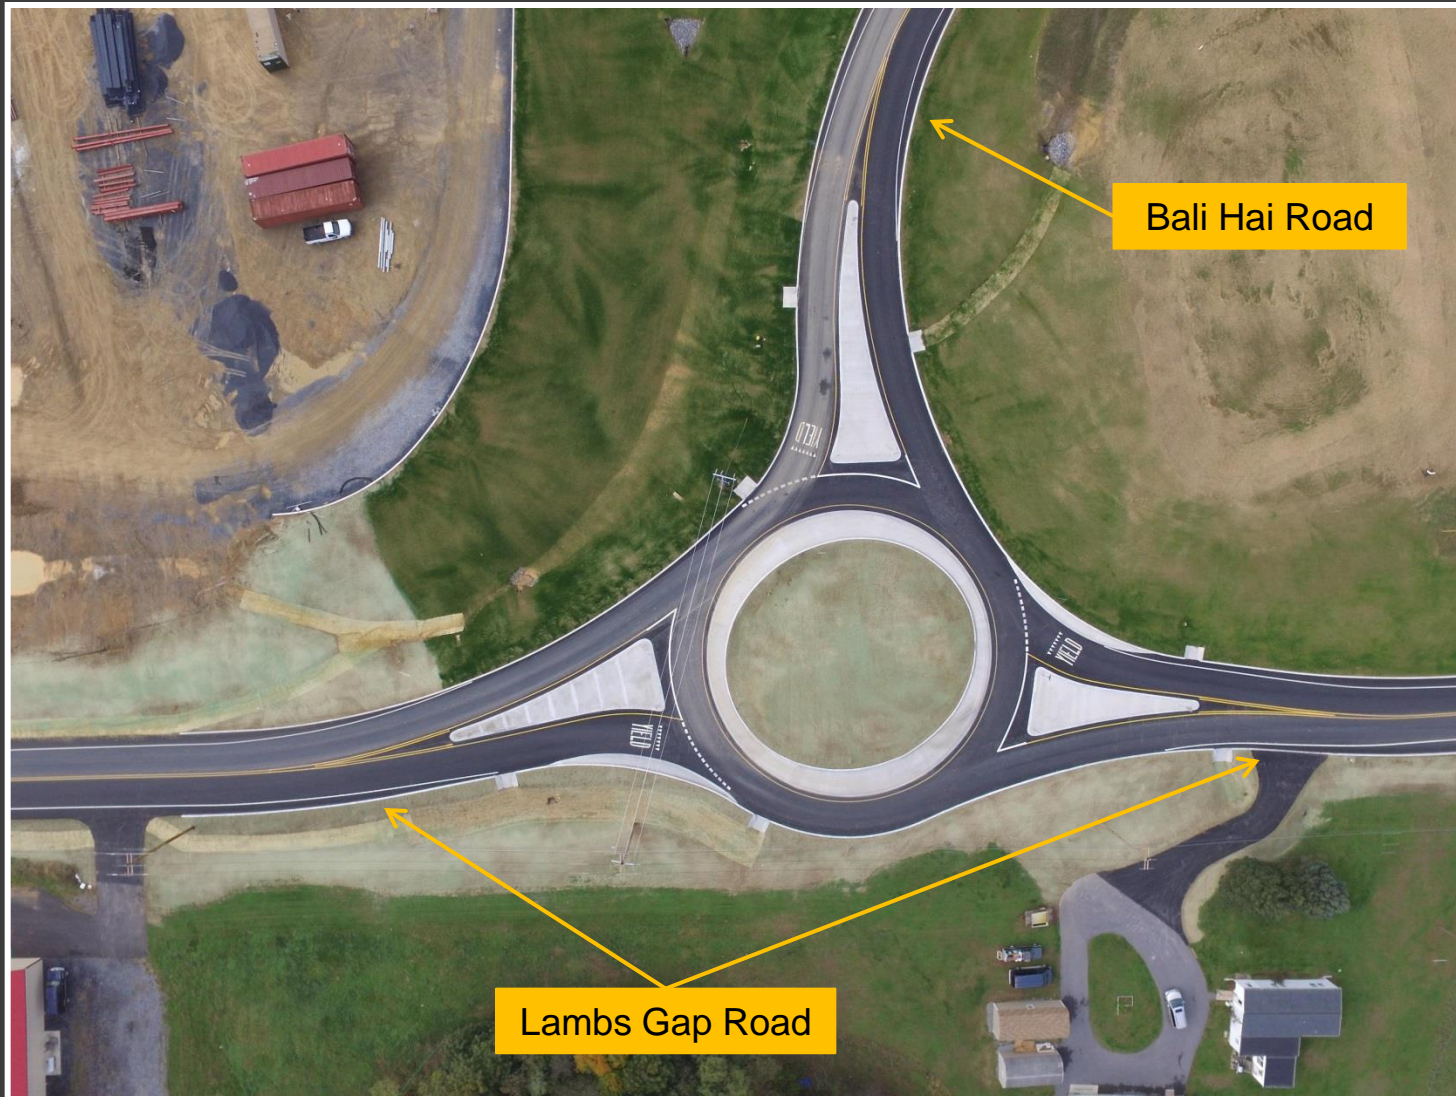

Bali Hai Road and Roundabout Opening

Bali Hai Road

Lambs Gap Road

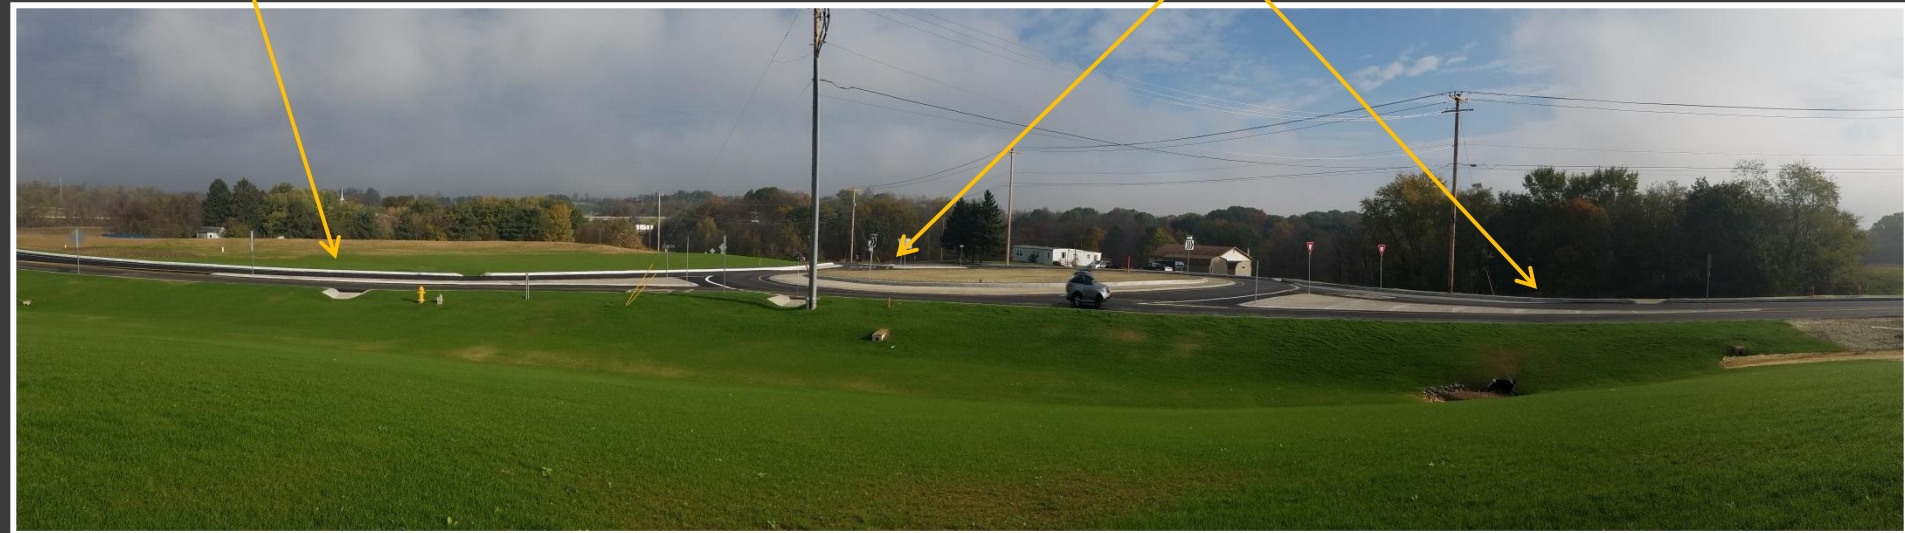

On 10/30/17, the relocated Bali Hai Road and new Roundabout were opened up to public traffic



CRABTREE, ROHRBAUGH & ASSOCIATES
ARCHITECTS



CUMBERLAND VALLEY
SCHOOL DISTRICT



Massaro
CONSTRUCTION MANAGEMENT SERVICES, LLC

Site Work



York Excavating placing stone subbase
for the Middle School parking area

Aerial Progress View



Mountain View Middle
School

Middle School Parking Lot

Additional Parking Lot

Stadium



CRABTREE, ROHRBAUGH & ASSOCIATES
ARCHITECTS



Massaro
CONSTRUCTION MANAGEMENT SERVICES, LLC

Aerial Progress View

Area C – Masonry has started; MEP rough-ins ongoing

Area B – Masonry up to 2nd floor window sill; 2nd floor joists are being installed

Area A – Masonry up to 2nd floor window sill; joist and decking ongoing

Areas D & E – Footings now complete; underslab rough-ins ongoing



Photo taken by MCMS on 11/02/17



CRABTREE, ROHRBAUGH & ASSOCIATES
ARCHITECTS



Massaro
CONSTRUCTION MANAGEMENT SERVICES, LLC

Main Street



Main Street slab on grade has been placed



CRABTREE, ROHRBAUGH & ASSOCIATES
ARCHITECTS



Massaro
CONSTRUCTION MANAGEMENT SERVICES, LLC

Area A - Steel



2nd floor decking and structural steel install ongoing in Area A



CRABTREE, ROHRBAUGH & ASSOCIATES
ARCHITECTS



Massaro
CONSTRUCTION MANAGEMENT SERVICES, LLC

Area B – Rough-Ins



Ductwork prepped in Area B for install in coordination with wall install



CRABTREE, ROHRBAUGH & ASSOCIATES
ARCHITECTS



Massaro
CONSTRUCTION MANAGEMENT SERVICES, LLC

Area C - Masonry



1st floor masonry walls and door frames being installed in Area C



CRABTREE, ROHRBAUGH & ASSOCIATES
ARCHITECTS



Massaro
CONSTRUCTION MANAGEMENT SERVICES, LLC

Area C - Rough-Ins



Plumbing and electrical rough-ins are ongoing in Area C with the wall install



CRABTREE, ROHRBAUGH & ASSOCIATES
ARCHITECTS



Massaro
CONSTRUCTION MANAGEMENT SERVICES, LLC

Two Week Look Ahead

- York Excavating – Complete placing stone base at parking area and place asphalt paving
- Lobar – Continue 2nd floor bearing steel & decking in Areas A & B and continue 1st floor block work in Area C
- Silvertip – Continue plumbing rough-ins with ongoing block work Area A, B, & C and continue underground plumbing rough-ins in Areas D & E
- Boro – Continue electrical conduit rough-ins with ongoing block work in Areas A, B, & C and continue underground rough-ins in Area D & E
- Farfield – Continue wall sleeve layout in Area A & B with ongoing block work

